


Apparel & Footwear

Link Project Critical Path Activity to Production JOB


Link Project Critical Path Activity to Production JOB

It is possible to track a production activity in the critical path. This is by relating the two activities. If the production task is delayed the critical path gets updated automatically.

Important: make sure you don't have the allow overlapping activities active in the setup.

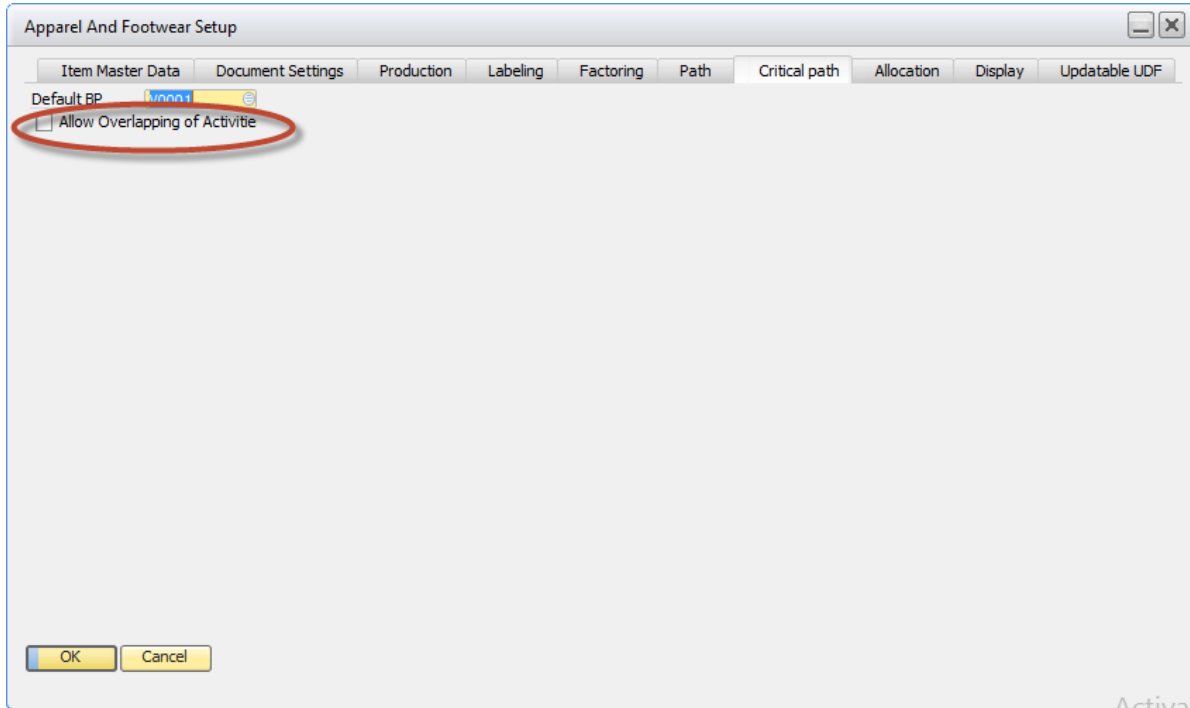

Create a style with a workflow, then create a project

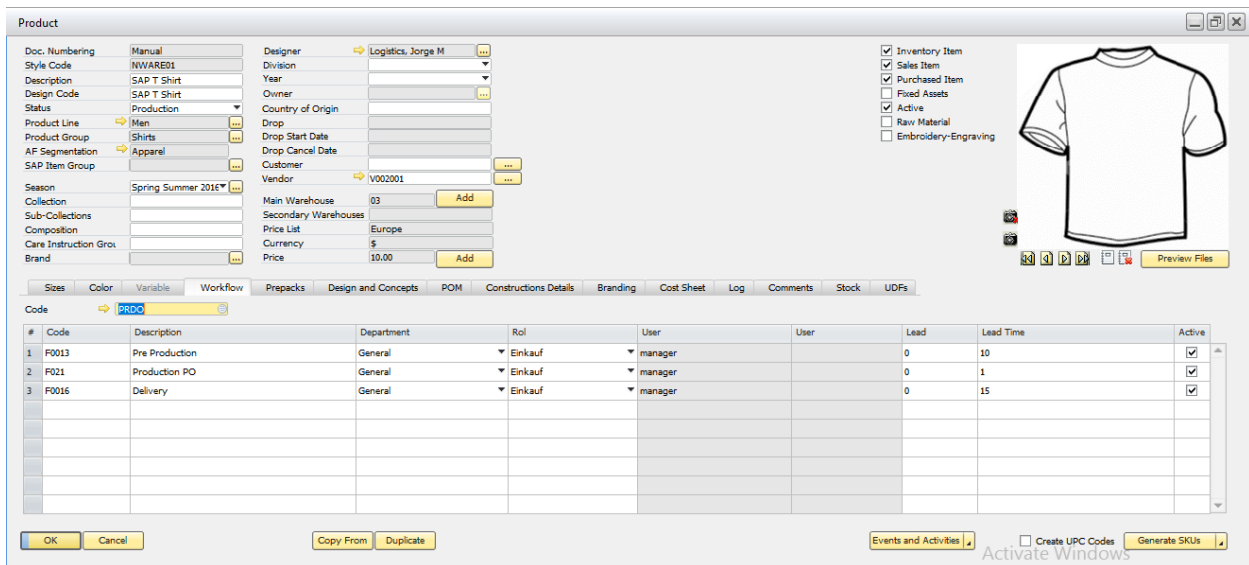

Assign the JOB number to the critical path activity

The screenshot shows the 'Critical path' window in SAP. The main table lists activities with columns for #, Planned Date, and Planned date to. An overlaid dialog box titled 'List of ArgnsSendOut' shows a table with columns #, Doc, Operation, and Description. A red arrow points from the 'Send Out' activity in the dialog to the corresponding row in the main table.

#	Planned Date	Planned date to	SAP A...	Priority	Comments	Job DocNum
1	09/30/16	10/14/16	607	Normal	NWARE01 -	
2	10/14/16	10/17/16	608	Normal	NWARE01 -	
3	10/17/16	11/07/16	608	Normal	NWARE01 -	

#	Doc	Operation	Description
1	602	OP002	Send Out

The activity shows in the production JOB

The screenshot shows the 'Job' window in SAP. The 'Send Out' tab is selected, displaying a table with columns for #, Item Code, Item Description, and Bar Code.

#	Item Code	Item Description	Bar Code
1	NWARE01-334-S	SAP T Shirt Moss Small	00
2	NWARE01-334-M	SAP T Shirt Moss Medium	00
3	NWARE01-334-L	SAP T Shirt Moss Large	00

If the planning in production is updated. The critical activity in the project is also updated

Critical path

Code: 268-NWARE01-112
 Description: NWARE01
 Model Code: NWARE01
 Model: SAP T-Shirt
 Workflow: PRDO
 Compare Planning

Status: In progress
 Calendar: 2013 Holidays
 Plan: Forward plan
 Date: 09/30/16
 Document Type: Document

#	Updated	W...	De...	Dep...	Ro	User	Employee	B...	Lead Time(Planned)	Lead Time(C...	Lead	Date From(Planned)	Date To(Planned)	Planned Date	Planned date to	SAP A...	Priority	Comments	Job DocNum
1		F0013	Pre Pr	Gen	Ei	manag		V000	10.000	10.000	0.000	09/30/16	10/14/16	09/30/16	10/14/16	607	Normal	NWARE01 -	
2		F021	Produ	Gen	Ei	manag		V000	1.000	1.000	0.000	10/14/16	10/17/16	10/14/16	10/17/16	608	Normal	NWARE01 -	602
3		F0016	Deliver	Gen	Ei	manag		V000	15.000	15.000									

Activity

Activity: Task
 Type: General
 Subject: Vendor
 Assigned To: manager
 Assigned By: manager
 Number: 608
 BP Code: V0001
 BP Name: GOMODA
 Contact Person:
 Telephone No.:

Remarks: NWARE01 - Production PO
 Start Time: 09/25/16 8:00AM
 End Time: 09/30/16 3:00AM
 Duration: 5 Days
 Status: Not Started
 Priority: Normal
 Meeting Location:
 Recurrence: None

Buttons: Update, Cancel, Calculate

Save Cancel Model View User View Print Activities Dependency

ID	Task Name	Start	End	Duration	Planned Start	Planned End
1	F0013 - Pre Production	30/09/2016	14/10/2016	10	30/09/2016	14/10/2016
2	F021 - Production PO	28/10/2016	29/10/2016	1	14/10/2016	17/10/2016
3	F0016 - Delivery	29/10/2016	19/11/2016	16	17/10/2016	07/11/2016

Task Name: F021 - Production PO
 Start: 10/28/2016 12:00:00 AM
 End: 10/29/2016 12:00:00 AM
 Job: 603
